

The recovery spending watchdog №22: Reconstruction of Ukraine

#22, September 2025

brp.org.ua



Content

- Legal regulation
- Recovery process and funding
- 2026 State budget review: reconstruction and recovery funding
- Analysis of recovery procurement
- Monitoring specific areas: housing, education, healthcare



Legal and regulatory framework



Increased transparency in allocating funds from the State Fund for Regional Development (SFRD)

SFRD funds allocation transparency and precision was increased

The government has approved the procedure for the use of funds from the State Fund for Regional Development (SFRD) ([Cabinet of Ministers Resolution No. 971](#)), which outlines how the 1 billion UAH allocated to the SRDF for 2025 will be distributed.

- As before, the Ministry of Development will be the program's manager.
- The approach to financing and implementing projects with SFRD funds has changed: now, it involves public investment projects, and accordingly, the preparation and selection process must meet the requirements for public investment projects.
- All applications must be entered into the Unified Project Portfolio and align with national priorities. They are submitted through the DREAM platform, which makes the selection process more transparent and ensures that the funds are directed to priority areas in line with the strategy.
- Projects undergo prioritization through an automatic system embedded in DREAM, based on criteria defined by the government for public investment projects. The final decision is made by a commission that includes representatives not only from ministries but also from civil society.
- Prioritization is carried out based on a clear scoring system established in the Resolution. According to it, priority is given to projects whose documentation was prepared after November 15, 2023, projects where work has already begun and will be completed by the end of 2025, those implemented in poorer communities, and those that have adopted territorial development strategies.

Legislative changes: less bureaucracy in procurement, fewer barriers for people with limited mobility.

New buildings will become more accessible for people with limited mobility: [inclusive construction standards have been updated](#). Changes to the DBN (State Building Norms) “Inclusivity of buildings and structures” have come into force, setting modern requirements for entrances, ramps, doors, and tactile strips. Now, every new facility must be convenient and safe for everyone, including people with limited mobility.

Energy facilities will be restored faster: procurement processes in construction have been simplified to speed up the reconstruction efforts. The government has updated the public procurement rules in the construction and restoration of energy facilities ([Cabinet of Ministers Resolution No. 1067](#)). Instead of lengthy bureaucratic procedures, work will start faster with digital control tools. This is expected to accelerate recovery and make the process more transparent for communities and contractors.



Housing for IDPs is to become more affordable

- **Remote assessment of destroyed housing is now possible even in combat zones**: The government has approved a decree allowing commissions to remotely assess destroyed housing in areas of potential military conflict. This simplifies and expands the mechanism for assisting IDPs under the eRecovery program, accelerating the issuance of housing certificates.
- **The government is expanding access to the eShelter program for IDPs and residents of frontline areas**: Starting September 10, 2025, an updated mechanism for the program will be launched, enabling residents of frontline regions and IDPs without housing in government-controlled territories to have greater access to housing. These categories will be able to receive a 70% compensation for the first installment (but no more than 30% of the housing cost) and up to 70% of the monthly payment for the first year (under the eShelter program, typically only partial compensation is provided). These changes are an important part of housing support during the war.
- **Funds from temporarily occupied communities will be redirected for housing for IDPs**: This is specified in the draft 2026 State Budget under article 42. The funds will be transferred to a special fund and used for providing housing for IDPs.



The UAH 11 trillion Unified Project Portfolio was approved

The Rapid Implementation Readiness Assessment (RIRA) has begun: The RIRA (Rapid Implementation Readiness Assessment) project has commenced to assess the readiness of state and local institutions to work on projects from the Unified Project Portfolio. The assessment covers management, procurement, finances, and engineering and technical aspects. The project is being implemented by PwC Ukraine with financial support from the EBRD and the UK Foreign, Commonwealth & Development Office.

The Unified Project Portfolio (UPP) for 2026 has been approved: The Strategic Investment Council has approved the UPP-2026, the main document for implementing the Mid-Term Investment Plan. This marks the official start for preparing projects that will be financed in 2026 (more details in the "Recovery process and funding" section) – communities have submitted projects worth UAH 11 trillion. For comparison, total state budget revenues for 2026 are planned to be around UAH 3 trillion, so funding will not be allocated to all projects in 2026.

Ministry of Development and the DREAM office continue training in the regions: Communities and regions are being engaged in the public investment management reform, so the Ministry of Development and other institutions continue with training and informational meetings. The "Five Case Model" methodology is used to prepare high-quality applications for UPP-2026.

MFIs will continue to fund recovery and development programs: The Ministry of Development and the EIB discussed the investment project portfolio and new infrastructure initiatives. Meanwhile, the Ministry of Development and the IFC (International Finance Corporation) have agreed to strengthen cooperation in the area of public-private partnerships.

Recovery progress and funding



Four months before the end of the year, the project selection for SFRD is not yet finalized

On August 26, the Ministry of Development announced the selection of projects for financing from the State Fund for Regional Development (SFRD): communities were required to submit their projects through DREAM from September 1 to 10 (which are quite tight deadlines). The next step will be the consideration of projects by the Interdepartmental Commission, taking prioritization into account. As of the end of September, projects for 2025 have not yet been determined.

- The allocation of funds just a few months before the end of the year raises concerns about the potential issues with the timely completion of projects this year. Therefore, priority is given to projects exceeding UAH 70 million, for which tenders have been completed, contracts signed, and implementation will be completed by 2025 (otherwise, the funds will be "lost" and unavailable for future use).
- New approaches, approved for public investment projects (PIP), are already being applied to the allocation of funding from the State Fund for Regional Development (SFRD).
- Total funding: UAH 1 billion. The planned distribution is UAH 500 million for frontline areas, UAH 300 million for central regions, and UAH 200 million for rear regions.
- The priorities are quite broad: education, healthcare, municipal infrastructure, civil protection, and public services.
- 200 projects from 22 regions are awaiting review: they have already gone through automatic prioritization via the DREAM system.

Number of received applications



Source: DREAM

Projects recorded in DREAM, submitted for SFRD financing:

- 88 education and science,
- 46 healthcare,
- 35 municipal infrastructure,
- 10 social security,
- 7 social spending,
- 4 environment,
- 3 housing

The majority of projects in the formed UPP comes from large state companies


The Strategic Investment Council approved the new Unified Project Portfolio (UPP) — the total financing amounts to UAH 11.4 trillion, representing the full life-cycle cost of projects (design, construction, and subsequent maintenance) for the coming years:

- 89 projects totaling UAH 7.3 trillion
 - Project status: 60 – investment feasibility study (technical and economic reasoning), 29 – preliminary investment feasibility study (technical and economic reasoning)
 - 32 project initiators: Ministry of Development – 12 projects, Ukrzaliznytsia – 12 projects, Ukrhydroenergo – 9 projects, Ukrenergo – 7 projects
 - 60 programs totaling UAH 4.1 trillion
 - 8 program initiators: Ministry of Development – 26 programs, Ministry of Health – 11 programs, Recovery Agency – 10 programs

The Unified Project Portfolio was formed based on the approved indicators of the 2026–2028 Budget Declaration and the Medium-Term Plan of Priority Public Investments of the state for 2026–2028:

- ✓ According to these documents, a Consolidated List of Programs and Projects of the UPP was created;
- ✓ Currently, the figures that the government plans to include in the budget (from both own revenues and multilateral financial organizations) are known. It has been determined that the financing of UPP projects and programs for 2026–2028 will amount to UAH 229 billion.

UPP financing by the state budget, UAH billion

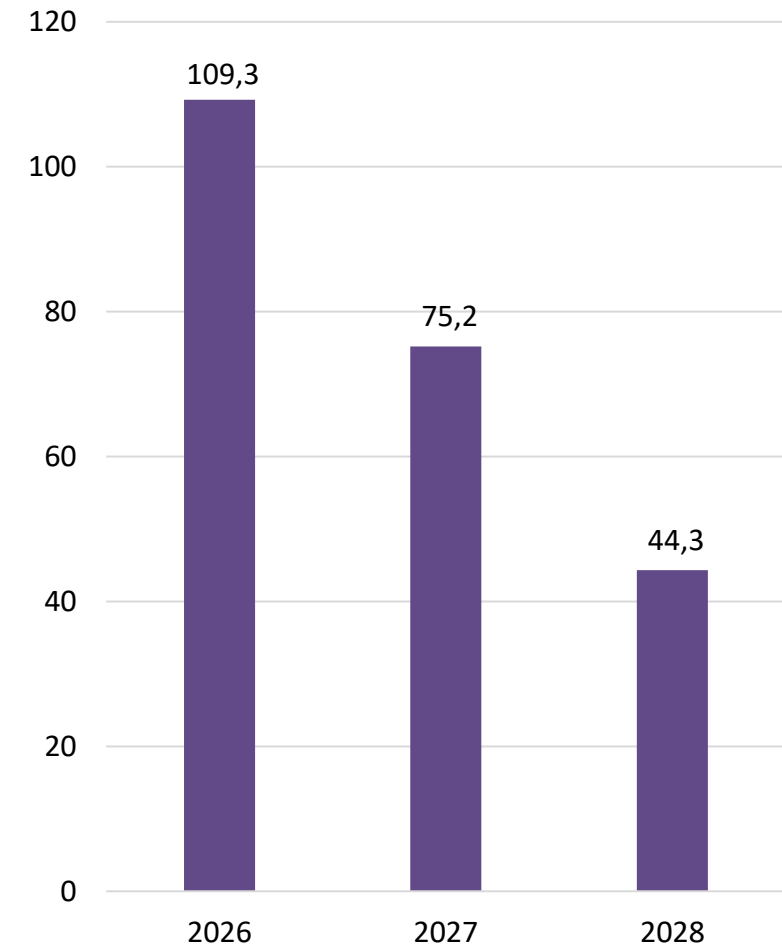

How is UPP going to work? Explanation by the Deputy Minister of Development



In the Unified Project Portfolio (UPP), programs and projects are distinguished. As explained by Deputy Minister of Development, Marina Denysiuk (these terms are more comprehensively defined in the Budget Code):

- **Public investment project (PIP)** is a separate initiative within a specific sector, such as building a water supply system, upgrading passenger trains, or constructing infrastructure as part of integration into the Trans-European Transport Network (however, PIP does not include activities related to the country's defense capabilities).
- **Public investment program** is a set of several projects with a common goal. For example, numerous projects for insulation and equipping schools with generators are grouped under one energy efficiency program. Meanwhile, large infrastructure projects may exist outside of program.

In the budget, the category "**Development expenditures**" includes both investment projects and programs, as well as other capital operations, such as the acquisition of fixed assets, construction/reconstruction, capital repairs, and separate capital transfers. The expected useful life of the corresponding fixed assets does not exceed one year, and the projects are limited to a specific investment object.



The majority of projects in UPP are municipal infrastructure and services, but the main financing is directed towards the energy sector

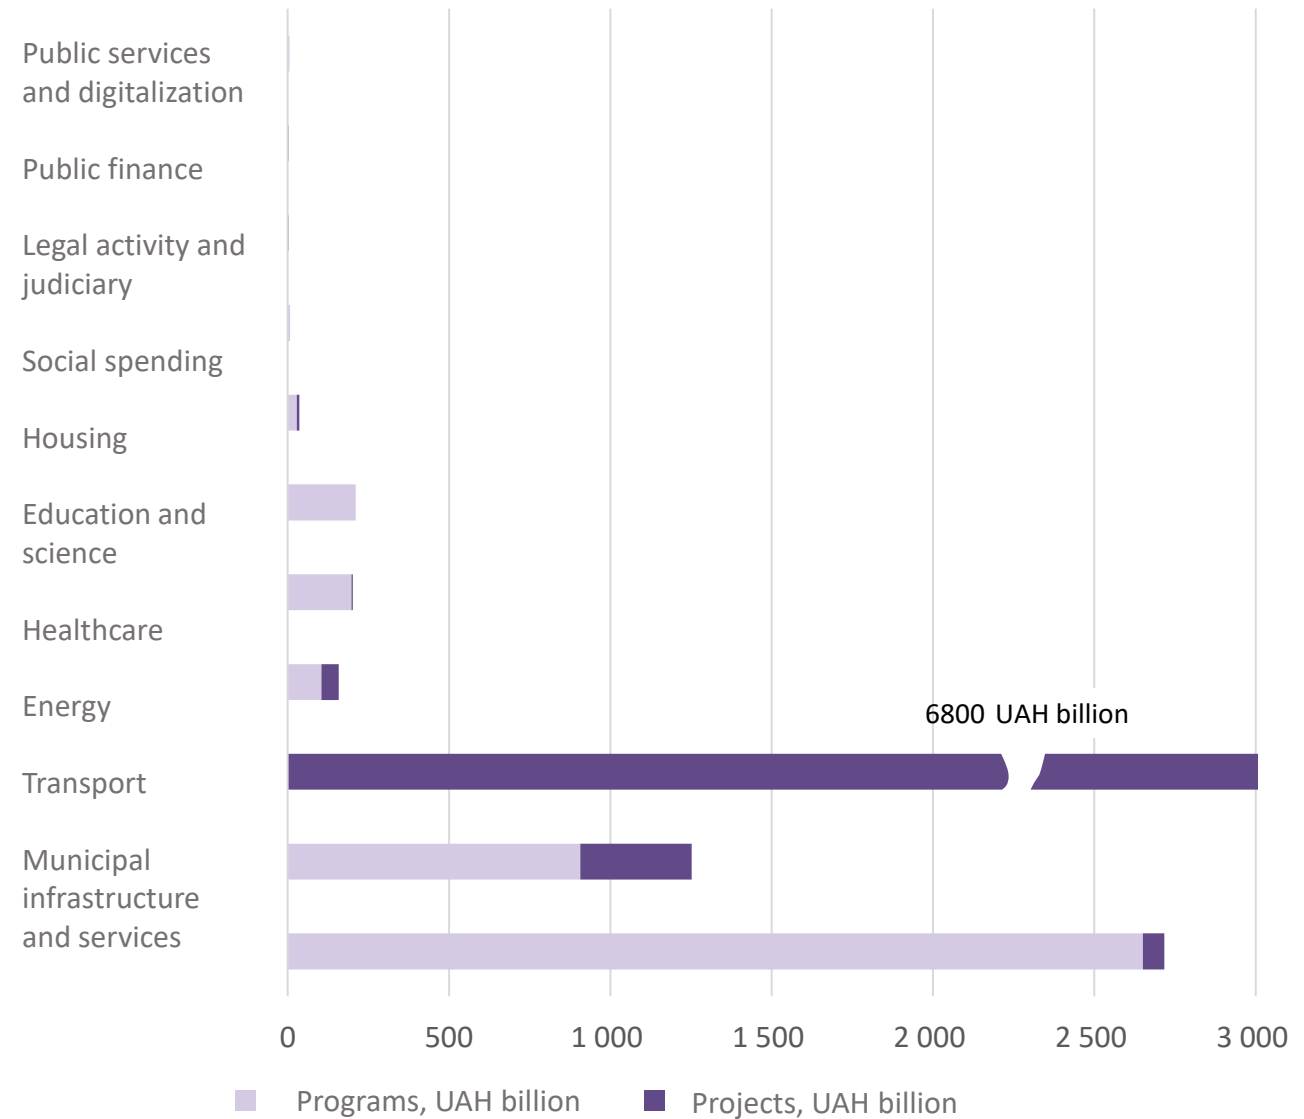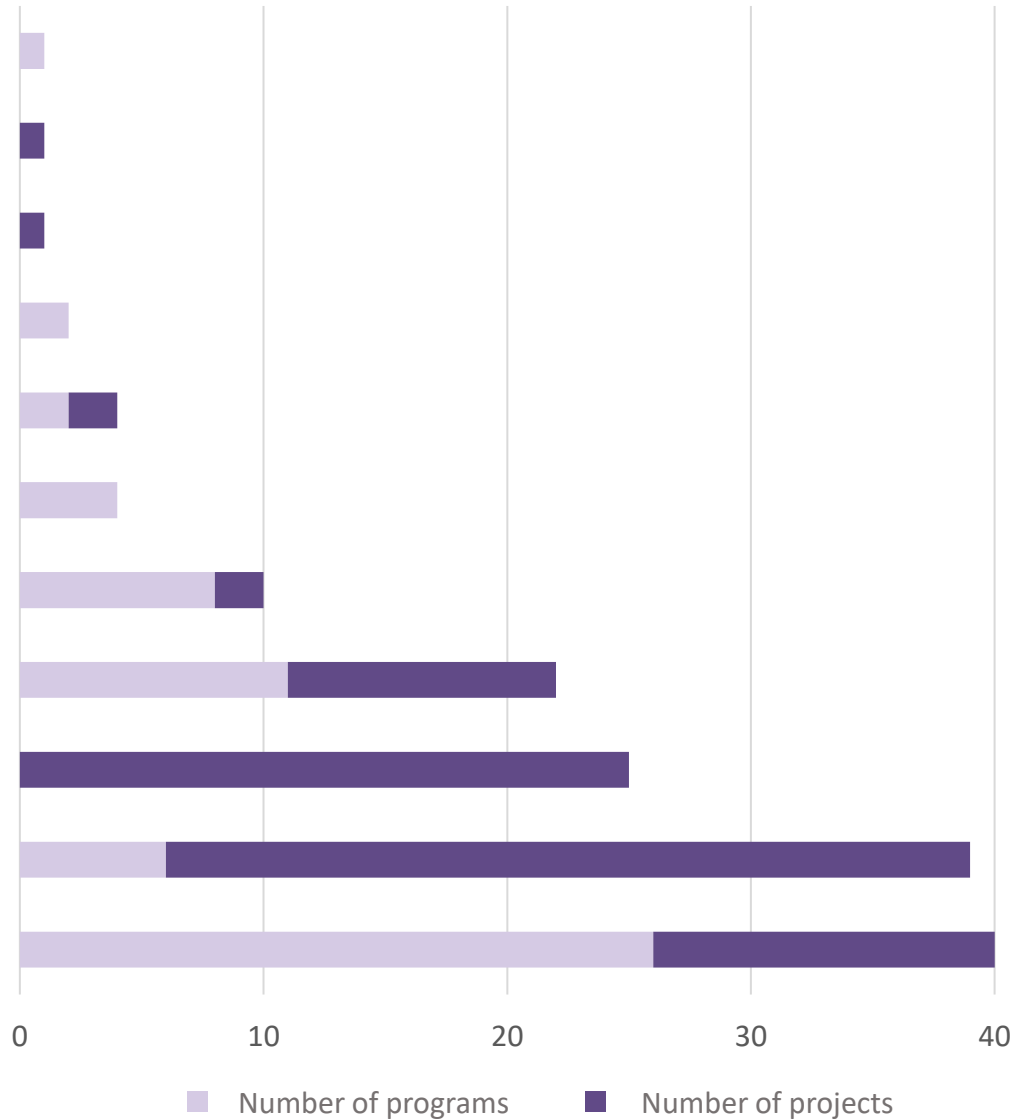

2026 State Budget review: reconstruction and recovery funding



Public investment projects will be financed from the budget with UAH 109 billion, primarily through loans from international financial organizations (IFOs).

The State budget draft considers the implementation of the public investment reform.

Funding for public investment projects (PIPs) approved for 2026 by the Strategic Investment Council:

- **UAH109 billion** (of which UAH **30 billion** are from the general fund, UAH **57 billion** from the special fund, and UAH **22 billion** from state guarantees) will be allocated to the implementation of **66** public investment projects and programs across **11** sectors (industries). The special fund will be financed by IFOs.

At the same time, IFO funding needs to be raised not only for public investment projects. According to the explanatory note, a total of UAH **115** billion (in equivalent) will be mobilized from loans from other countries and MFOs for all infrastructure projects (including PIPs) and fortification construction, with UAH **57** billion allocated specifically for PIPs. Some of this has already been covered by existing agreements with MFOs, but not all, meaning Ukraine needs to seek new funding and expand current programs.

Therefore, according to the State Budget project, reconstruction and recovery will once again primarily rely on loans, and the available funding remains limited and insufficient for the necessary needs.

Hence, the **prioritization of projects and the efficient implementation of public investment projects** is critically important.

The largest number of PIPs is within the responsibility of the Ministry of Development

PIP domain	Number of programs and projects	Total, UAH million	Main Funds Disburser
EEnergy	7	34,784	Ministry of Energy, Ministry of Development
Transportation	15	23,323	Ministry of Development, Recovery Agency
Healthcare	14	18,550	Ministry of Healthcare, State Affairs Administration, National Academy of Medical Sciences of Ukraine
Science and education	9	15,017	Ministry of Education and Science
Municipal infrastructure and services	11	8,769	Ministry of Development
Social spending	4	5,686	Ministry of Social Policy, Ministry of Veteran Affairs
Social services and related digitalization	1	800	Ministry of Digital Transformation
Legal Activity and Judiciary	1	787	Ministry of Justice
Public finance	1	688	Ministry of Finance
Housing	1	627	Ministry of Development
Environment	2	226	Ministry of Economy, Ministry of Energy

Source: 2026 Draft state budget annexes

Збільшується бюджетне фінансування програм відбудови та відновлення, розпорядником яких є Мінрозвитку

- In 2026, funding for reconstruction and recovery programs, with the **Ministry of Development** as the main funds disburser, is increasing:
 - ✓ It is important to note that the increase primarily concerns the general fund of the state budget, which highlights the urgency of recovery efforts.
 - ✓ The largest program is the implementation of Public Investment Projects (PIP): UAH 13.7 billion.
 - ✓ The Ministry of Development continues to prioritize comprehensive recovery: UAH 10 billion are planned for this.
 - ✓ For the eVidnovlennya program, less money is allocated from the special fund than expected (due to planning specifics), but UAH 3 billion are allocated from the general fund for compensation for damaged housing.
 - ✓ Funding for energy efficiency is increased, with UAH 630 million allocated to the Energy Efficiency Fund, which finances the EnergoDim program for housing reconstruction.
 - ✓ The housing lending program is expanding, including for youth.
- In 2026, the **Recovery Agency** effectively includes two programs: road construction and repairs, as well as debt servicing: the allocation for roads is rather small – UAH 12.6 billion, and for debt servicing – 15 UAH billion.

Reconstruction and Recovery expenditures*, UAH billion



Note: In the diagram, the programs of the Ministry of Development, which are assessed by the Institute for Economic Development (IED) as part of the Ministry of Development's reconstruction and recovery programs, are presented. The Agency includes recovery programs, roads, and debts servicing.

The largest programs of the Ministry of Development, funded from the general fund, are Public Investment Projects (PIP) and compensation for destroyed property.




UAH million	2025		2026		
	General Fund	Special Fund	General Fund	Special Fund	TOTAL
Ministry of Development of Communities and Territories of Ukraine	4 240.00	25 013.85	18 364.74	19 296.24	37 660.98
Public investment projects			13735		13735
Compensation for destroyed property	3000		3000		3000
Compensation for destroyed property within eVidnovlennya program	1000		1000	229	1229
Energy efficiency fund	240		630		630
Critical logistics and network connections (RELINC)		3434		6185	6185
Development of municipal passenger transport in Ukrainian cities		3866		4228	4228
Compensation for destroyed property (HOME)		462		2468	2468
Energy efficiency of civil buildings in Ukraine		2462		1858	1858
Ukrainian railways modernization		1217		1234	1234
Municipal infrastructure, water management in Mykolaiv and Chernivtsi		2456		946	946
Danube Logistics (RELINC)		1389		940	940
Development of municipal infrastructure		9411		790	790
Energy efficiency of civil buildings		63		265	265
Water supply and wastewater management in Mykolaiv		146		71	71
Housing Repair for People's Empowerment (HOPE)		63		42	42
Credits for construction (reconstruction) in villages and housing procurements		32		33	33
Preparing the energy system for winter		15		8	8
Port infrastructure projects				1	1

Notes: the programs are chosen in relation to reconstruction, recovery and construction

Source: 2026 Draft state budget annexes

Subsidies for the Ministry of Development programs – mainly funded by International Financial Organizations (IFOs)

- In 2026, funding for the State Fund for Regional Development (SFRD) is set at UAH 2 billion (compared to UAH 1 billion in 2025, see slide 9) from the general fund of the state budget:
 - ✓ The Budget Code provision, which mandates that SFRD funding should be no less than 1.5% of the projected general fund revenue (UAH 39 billion), has been suspended due to the war;
 - ✓ SFRD will allocate funds based on projects submitted by local communities via the DREAM platform, as in 2025.
- Subsidies from the Ministry of Development from the special fund will mainly depend on the availability of funds from international financial organizations (IFOs). These are programs for local reconstruction and recovery:
 - ✓ Most of the funding will come from the European Investment Bank and the World Bank;
 - ✓ Key conditions for efficient use of funds:
 - Absorptive capacity of local communities;
 - Timely tendering processes for procurement.
- Plans for building metro systems in Dnipro and Kharkiv remain, though they are currently also used as shelters during air raid alerts.

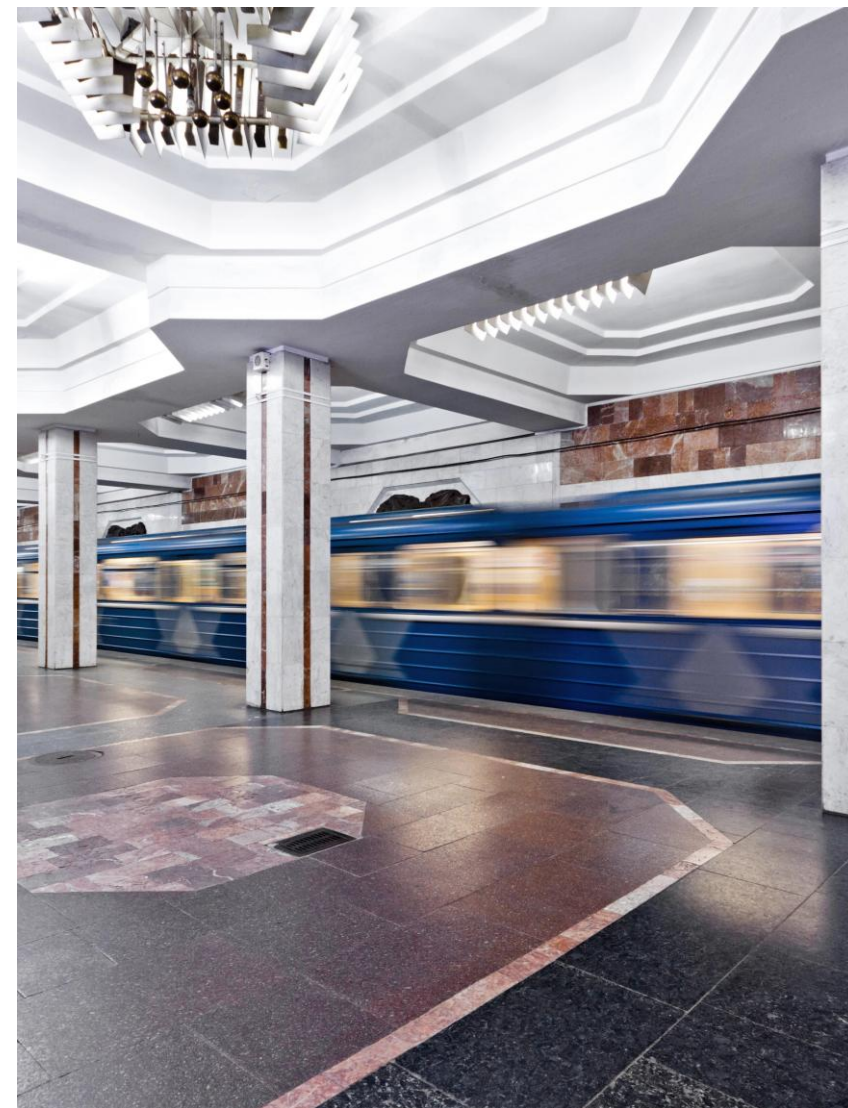

Subsidies for the Ministry of Development programs – mainly funded by International Financial Organizations (IFOs).

UAH million	2025		2026		
	General fund	Special fund	General fund	Special fund	BOTAL
Subsidies of the Ministry of Development	1 140.40	13 100.70	2 135.00	5 836.30	7 971.30
Subsidy from the state budget to local budgets for the implementation of projects under the Emergency Credit Program for the Recovery of Ukraine		1551		2734	2734
DeState fund for regional development	1000		2000		2000
Subsidy from the state budget to local budgets for the implementation of projects under the Emergency Credit Program for the Recovery of Ukraine II		5000		987	987
Subsidy from the state budget to local budgets for the implementation of projects under the Emergency Credit Program for the Recovery of Ukraine III		1000		740	740
Subsidy from the state budget to the Dnipro municipal territorial community for completing the metro line construction in the city of Dnipro	140	702	135	500	635
Subsidy from the state budget to the local budgets for the implementation of the project «Housing Repair for People’s Empowerment (HOPE)»		540		357	357
Third metro line extension in Kharkiv		2090		259	259
Subsidy from the state budget to the Dnipro municipal territorial community for completing the third metro line construction in the city of Kharkiv		2090		259	259
Subsidy from the state budget to the local budgets for the reconstruction of critical infrastructure objects within the project “Municipal reconstruction project – 2” supported by the International Bank for Reconstruction and Development.		127			0

Analysis of recovery procurement as of August 2025*


*operative data as of 11.09.2025,
may be specified




In 2025, the number of construction procurements* steadily increased compared to the previous year

- The vast majority of the procurements announced in August 2025 have already been completed — 11,000 (82%). Another 12% are still ongoing, 5% have not occurred, and 1% were canceled.
- The largest completed procurement in August 2025 is the project for the construction of power transmission lines in the Odesa region, worth UAH 622.6 million. The works are being carried out by "Struktum LLC."
- The largest organizer in August 2025 is "Ukrenergo PJSC" with a total value of UAH 863.3 million, including the reconstruction of energy facilities to prepare for the heating season.

The number of announced construction procurements has risen in August...

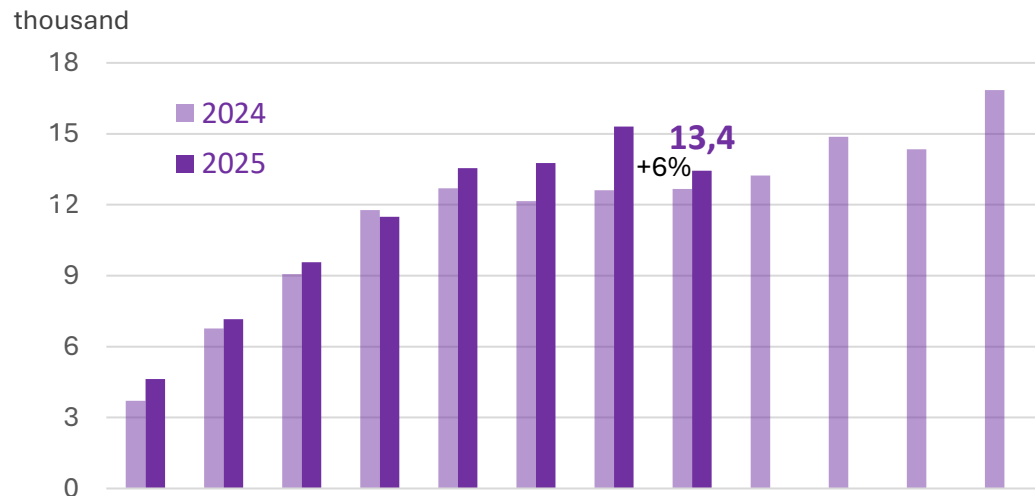


...but the total amount of announced procurements has dropped

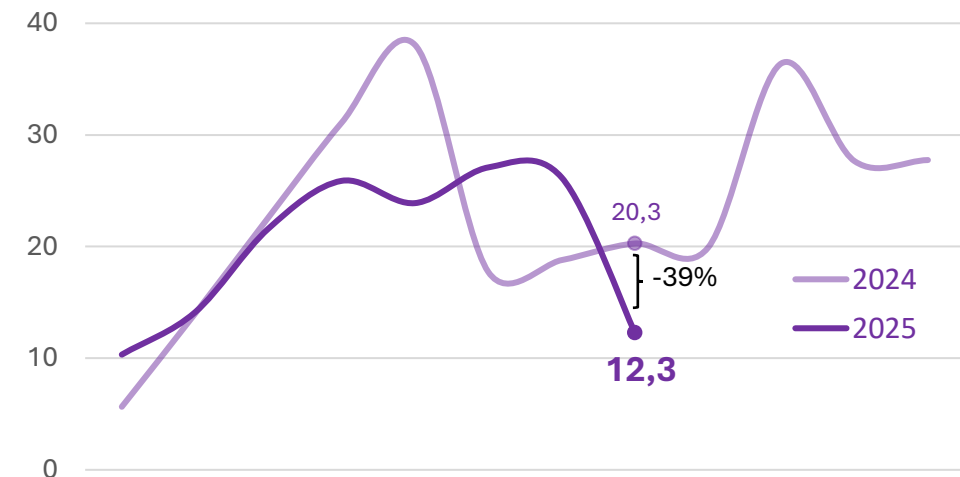

A significant portion of construction procurements* takes place outside the electronic system

- The electronic system was used only for 1000 completed procurements (10% of all completed) worth UAH 2.9 billion (35% of all procurements) in August 2025.
- In August 2025, procurements without the use of the electronic system (basic procurements) consistently took the leading position in terms of the total value of completed procurements – around UAH 5.2 billion, while the number of such completed procurements was 9800 (89% of all procurements).


The majority of procurements in August 2025 took place outside of the electronic system

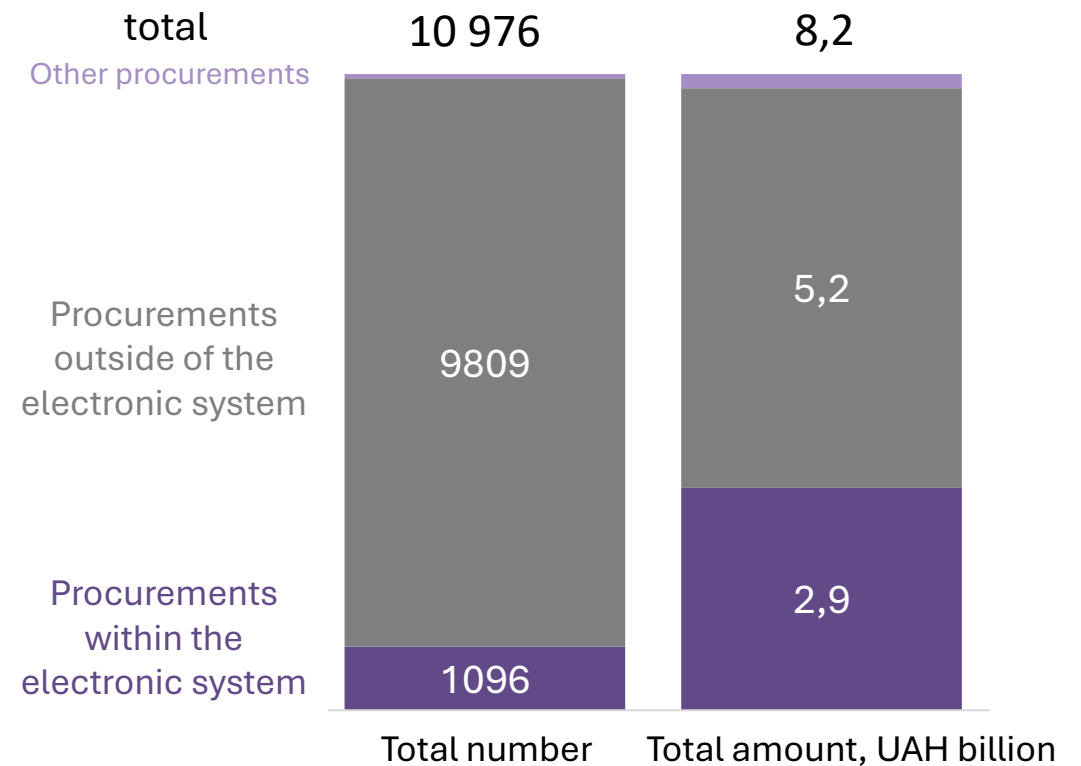

* Construction and ongoing reconstruction procurements

The first place in construction procurements* in August was occupied by both the organizer and the winner of projects in the energy sector


Top 10 organizers (UAH billion)

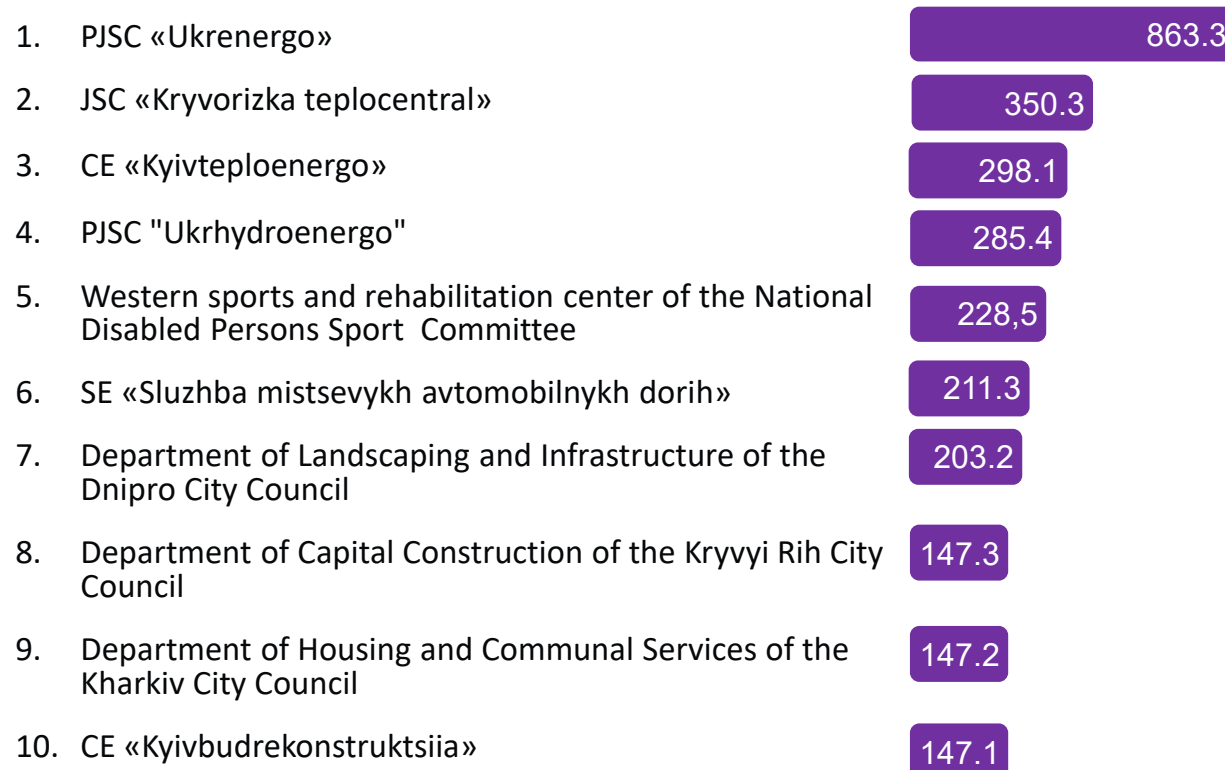

The share of the top 10 in all procurements



Top 10 winners (UAH billion)

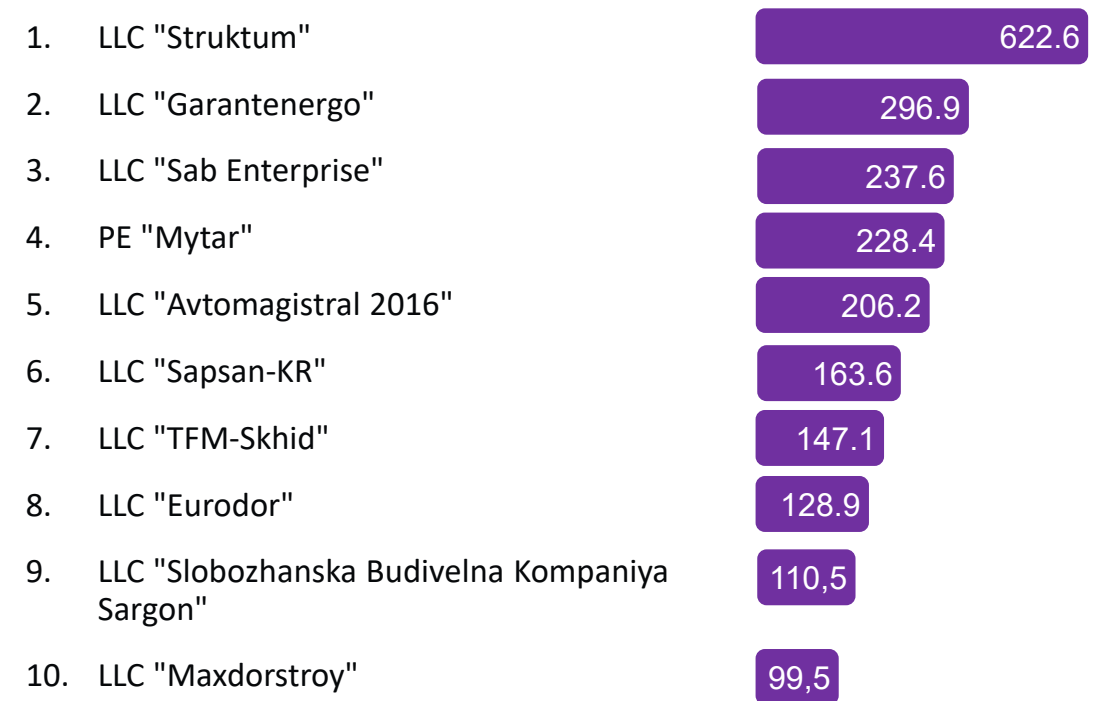

The share of the top 10 in all procurements




*construction and ongoing reconstruction procurements

The five largest construction procurements* in August were infrastructure projects, including energy projects

№ Procurement	Organizer	Winner	Procurement cost, UAH million
1. Project for the construction of power transmission lines in Odesa oblast	PJSC «Ukrenergo»	LLC «Struktum»	623
2. Reconstruction of the substation with the installation of physical protection of autotransformer	PJSC «Ukrenergo»	LLC «Sab Enterprise»	238
3. Ongoing repair of roads and streets in the city of Dnipro	Department of Urban Development and Infrastructure of Dnipro City Council	LLC «Avtomagistral 2016»	186
4. Additional works on the reconstruction of Bortnytskyi drainage dam	CE «Kyivbudrekonstruktsiya»	LLC «TFM-Skhid»	147
5. Additional works on the construction of structures for the protection of electrical equipment at the "Kaniv HES" branch	PJSC «Ukrhydroenergo»	LLC «Garant Energo»	141
6. New construction of a public building with a sports hall to create a veteran space in Kryvyi Rih	Department of Capital Construction of the Executive Committee of Kryvyi Rih City Council	LLC «Sapsan-KR»	132
7. New construction of cottage №3 for rehabilitation and sports groups of the 'Western Rehabilitation and Sports Center' of the National Committee for Sports of Disabled Persons of Ukraine in Lviv Region	Department of Construction in Kyiv	LLC «Group of companies «Avtostrada»»	114

"Procurements* with a single participant prevail

- In August, there was a high share of procurements with a single participant (90% of all procurements accounting for 84% of the total procurement amount) using the electronic system (more details in the Annex).
- For the period from January to August 2025, the share of procurements with a single participant amounted to 96% of the number of procurements and 78% of the total procurement amount (more details in the Annex).
- In August, there were 3 procurements with 5 participants (the procurement cost decreased on average by 32% compared to the expected cost) and 6 procurements with 4 participants (the procurement cost decreased on average by 8% compared to the expected cost).

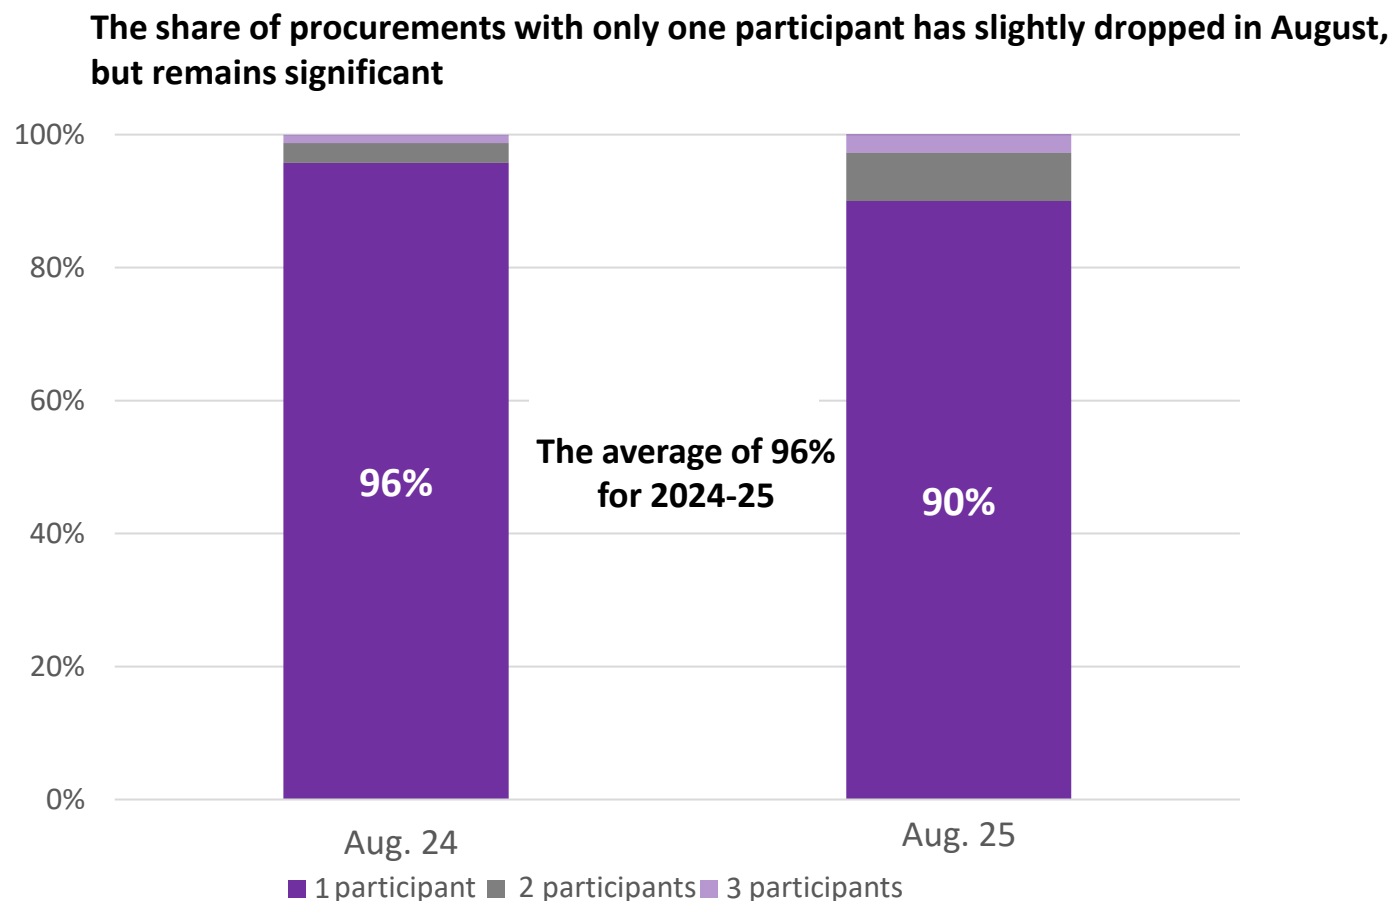

In procurements* with the highest number of participants, the price has significantly decreased

No	Procurement	Organizer	Winner	Cost, million UAH (expected/actual)		Participants
All procurements						
1.	Development of project documentation for the establishment of a truck parking lot	Service for the Recovery and Development of Infrastructure in Lviv Region	FPE Syphen T.M.	5.0 / 1.0	(-80%)	17
2.	Development of project documentation for the establishment of a truck parking lot	Service for the Recovery and Development of Infrastructure in Lviv Region	PP «Polissya-project»	4.0 / 1.2	(-70%)	17
3.	Ongoing repairs of the administrative building in Kyiv	National Bank of Ukraine	LLC «DIA GRUPP»	1.9 / 1.4.	(-26%)	13
Procurements with a value of more than UAH 20 million						
1.	Reconstruction of the cafeteria with the extension of the Kozeletskyi lyceum in Chernihiv region	Department of Education, Culture, Family, Youth, and Sports of Kozeletskyi Village Council	PE «Firma «Nominal»	40.4 / 36.7.	(-9%)	7
2.	Construction of a forest road in Vinnytsia region	State Forest Resources Agency "Forests of Ukraine"	PE «Avtomagistral»	34.3 / 23.4.	(-31%)	7
3.	Mining and technical reclamation works in the southern part of the "Verbolozivskyi" open-pit trench.	Ukrvuhlerestrukturyzatsiya	LLC «Montazhbudyg»	41.5 / 30.5	(-27%)	6

*construction and ongoing reconstruction procurements

Monitoring of specific areas

Healthcare

Education



Housing: Within the eVindovlennya program, compensation for damaged property is paid out more quickly, but at a lower rate than for destroyed property

- The number of applications for compensation for damaged housing and for housing certificates for destroyed property is increasing.
- The allocation and payment of compensation for damaged housing occur more quickly than in the case of destroyed housing.

	01.08.2025	01.09.2025
Damaged properties		
Total paid compensations	9.7	10.6
Number of applications	160,575	166,491
Number of decisions	141,728	146,844
Number of funded applications	97,637	108,037
Category A (small reconstructions)		
Funded applications	85,693	95,367
Paid, UAH billion	6.3	6.8
Average compensation amount, UAH	72,000	71,700
Category B (capital reconstructions)		
Funded applications, 1 st round	11,944	12,670
Funded applications, 2 nd round	6 020	6 505
1 st round funding amount, UAH billion	2.9	3.0
2 nd round funding amount, UAH billion	628.3	678.7
Average compensation amount, UAH	341,800	342,000

Source: Ministry of Recovery

	01.08.2025	01.09.2025
Destroyed properties		
Housing certificates		
Number of applications	57,527	64,030
Number of decisions of local self-governance bodies	27,890	29,337
Number of certificates issued by local self-governance bodies	21,400	22,763
Value of certificates issued by local self-governance bodies, UAH billion	31.1	33
Number of implemented certificates	12,902	15,018
Value of implemented certificates, UAH billion	20.6	23.6
Average certificate value, UAH million	1.5	1.4
Number of IDPs who successfully implemented the certificates	6,048	6,851
Value of certificates implemented by IDPs, UAH billion	8.3	9.4
Funding compensations for construction		
Number of applications	3,857	4,060
Number of decisions of local self-governance bodies	2,271	2,365
Number of positive decisions	956	968
Value of approving decisions, UAH billion	2.4	2.4
Number of financed solutions	580	632
Value of financed solutions, UAH billion	713.6	775.5
Average compensation value, UAH million	2.2	2.2

In August, on the DREAM platform the implementation of 1000 medical facilities projects is ongoing

- As of September 1, 2025, 2481 healthcare facilities have been either damaged or completely destroyed. Of these, 2155 facilities have sustained partial damage, while 326 have been fully destroyed. The regions most affected include Donetsk, Kharkiv, Luhansk, Chernihiv, and Dnipropetrovsk.
- 667 facilities have already been fully restored, 320 have been partially restored, and 50 have been restored but were damaged again.
- [As of September 1, 2025, capital reconstruction is ongoing at the Okhmatdyt medical and diagnostic complex](#): the facade is being updated and installed, new windows are being put in, lighting systems are being updated, internal work is being carried out, and engineering networks are being modernized.
- [The construction of an underground medical building](#) has started at the Kharkiv Regional Clinical Hospital to ensure continuous medical services during shelling.
- [There are already 1076 healthcare-related projects on the DREAM platform](#), including new construction and capital repairs.
- [During August 2025, 462 projects were added, with a total budget of UAH 240 billion \(financial coverage - 0.4%\)](#). The highest number of projects was implemented in Odesa (108), Ivano-Frankivsk (49), and Cherkasy (34) regions.



For the start of the academic year in Kyiv, 70% of educational institutions were recovered

- As of September 19, 2025, the following educational institutions have been damaged or destroyed:
 - 728 higher education institutions (including 553 with up to 50% damage and 175 with over 50% damage),
 - 2184 general secondary education institutions (schools) (including 1573 with up to 50% damage and 611 with over 50% damage),
 - 1298 preschool education institutions (including 1016 with up to 50% damage and 282 with over 50% damage).
- During this period, in various regions of Ukraine, **84 higher education institutions, 686 general secondary schools, and 404 preschool institutions have been fully restored and transferred to the balance sheet.**
- [As of August 2025, nearly 70% of educational institutions damaged by the war have been restored in Kyiv.](#) A total of 217 institutions were damaged. Alongside the restoration process, schools are being equipped with shelters.
- [On the DREAM platform, there are already 3,015 educational facilities under implementation](#)—new construction and capital repairs.
- In August 2025, 141 education projects were added, with a total budget of 3 billion UAH (financial coverage – 4.6%). The highest number of projects were in the Odesa (35) and Cherkasy (12) regions.



Annex

Number of participants	Number and % of procurements in January-August		Value (billion) and % of procurements in January-August		Number and % of procurements in August		Value (billion) and % of procurements in August	
1 participant	13,240	80.9%	79.2	70.6%	1050	90.0%	2.6	84.1%
2 participants	1933	11.8%	19.17	17.6%	85	7.3%	0.4	12.2%
3 participants	717	4.4%	8.4	7.5%	23	2.0%	0.08	2.6%
4 participants	252	1.5%	2.0	1.8%	6	0.5%	0.03	0.9%
5 participants	124	0.8%	2.5	2.2%	3	0.3%	0.0	0.15%
6 participants	54	0.3%	0.3	0.2%	0	0.0%	0.0	0.0%
7-17 participants	41	0.3%	0.2	0.2%	0	0.0%	0.0	0.0%
Total number of completed procurements within the electronic system	16.367	100.0%	112.2	100.0%	1 167	100.0%	3.1	100.0%



Thank you for your attention!

**Project «Recovery
spending watchdog»**

